FUNCTIONAL CONSUMPTION PLAN · SUMMARY

VMware Cloud Foundation Adoption: Acme Health

Version 1
Issued 30 Sep 2026
Prepared by CDW Consulting Solution Architecture

Platform: **VCF 9.1** · Path: **Greenfield with staging hardware** · Delivery: **CDW + Broadcom** · Location: **Reno, NV**

$79,403	223 hrs	1 Oct 2026	28 Apr 2027
VCF Services Entitlement	**Hours Remaining**	**Plan Starts**	**Entitlement Ends**
262 hours · 29 Apr 2026 to 28 Apr 2027	39 of 262 delivered as of 3 Sep 2026	Design and planning first; build from 1 Jan 2027	Unused hours are not refunded

WHAT WE'RE DOING

CDW designs and builds a new VCF 9.1 foundation for Acme Health on new hardware, proves the migration runbook on the first waves, and hands the platform and the runbook to Acme Health's team, who run the remaining waves. VCF Operations becomes the team's daily view of health and capacity. Recovery design and the first workload domain follow after the entitlement.

IN THIS PLAN

- **Program management:** kickoff and hardware compatibility review; assessment and discovery already delivered
- **Infrastructure:** design and bill of materials, foundation build, migration plan, proving waves
- **Operations:** VCF Operations design, access mapping, licensing, training, handover, runbook

NOT IN THIS PLAN

- **Cloud services:** Kubernetes, Private AI and HCX were not requested
- **Security and resilience:** recovery design and build follow in 2027
- **Remaining migration waves:** run by Acme Health with the runbook

ARCHITECTURE AT A GLANCE

Platform	VCF 9.1 on new Cisco UCS hosts. Converged management domain on the primary cluster, one VCF instance across the primary data center and the new DR site.
Storage, network	The existing NetApp array over Fibre Channel stays principal storage. NSX is deployed VLAN-backed at first; overlay networking is a later phase.
Recovery	The DR site joins as its own workload domain. The recovery design sets recovery objectives and the orchestration tool.

WORK PACKAGES

PACKAGE	MONTH	HOURS
DELIVERED TO DATE		
Assessment and discovery	*Jul to Sep 2026*	*39*
PROGRAM MANAGEMENT		
Hardware compatibility review	Oct 2026	15
Kickoff and delivery plan	Oct 2026	2
INFRASTRUCTURE		
Design and bill of materials	Nov 2026	24
Migration and cutover plan	Dec 2026	24
VCF foundation build	Jan 2027	61
Proving migration waves	Mar to Apr 2027	41
OPERATIONS		
VCF Operations design	Nov 2026	11
Role and access mapping	Dec 2026	15
Training and knowledge transfer	Jan 2027	6
VCF Operations licensing	Feb 2027	7
Handover and service acceptance	Apr 2027	11
Runbook knowledge transfer	Apr 2027	6
Total, funded by the entitlement		**262**

CDW-delivered hours: 39 delivered plus 223 planned equals the 262-hour entitlement. The signed resource assignments replace these estimates.

CDW · Proprietary and confidential. Copying restricted.

Timeline

1 October 2026 through 28 April 2027, the entitlement window. Dashed bars are run by Acme Health. Rounded bars mark key delivered functionality.

Governance · Infrastructure build · Migration · Operations · Run by Acme Health

Category	Oct 26	Nov 26	Dec 26	Jan 27	Feb 27	Mar 27	Apr 27
Program management	Kickoff and delivery plan Hardware sign-off						
Infrastructure	Close HCL evidence gaps	Design and BOM	Migration plan	VCF foundation build	Acme Health migration waves and legacy cluster retirement	Proving migration waves	
Operations		VCF Ops design	Role and access	Training	Licensing		Handover Runbook transfer
Cloud services	*Not in this plan*						
Security and resilience	*Recovery design and build follow after the entitlement*						

KEY DATES

1 Oct 2026	Design and planning start
30 Nov 2026	Acme Health decisions due: build hosts, DR direction, wave ownership
1 Jan 2027	Platform build begins
Apr 2027	Handover and service acceptance
28 Apr 2027	Entitlement ends; unused hours are not refunded

WHAT WE NEED FROM ACME HEALTH

- **Time:** about 7 hours a week through design and build, peaking at 30 hours a week (0.75 FTE) during your migration waves, Feb to Apr 2027.
- **Inventory:** a current RVTools export before the first design session.
- **Decisions by November:** hosts for the build, DR policy direction, wave ownership.

OPEN ITEMS

Current RVTools export	Gates design sign-off and sizing	Pat Rivera


AFTER THIS PLAN

> About **117 hours** of follow-on work runs from May 2027: the first workload domain, health and log monitoring, and recovery design and build. The two-year view is on page 3.

After the Entitlement

May 2027 through April 2028, the second year of the two-year view. This is where Acme Health goes next. None of it is funded by the current entitlement.

Governance · Infrastructure build · Operations · Consume and handover · Security and resilience · Run by Acme Health

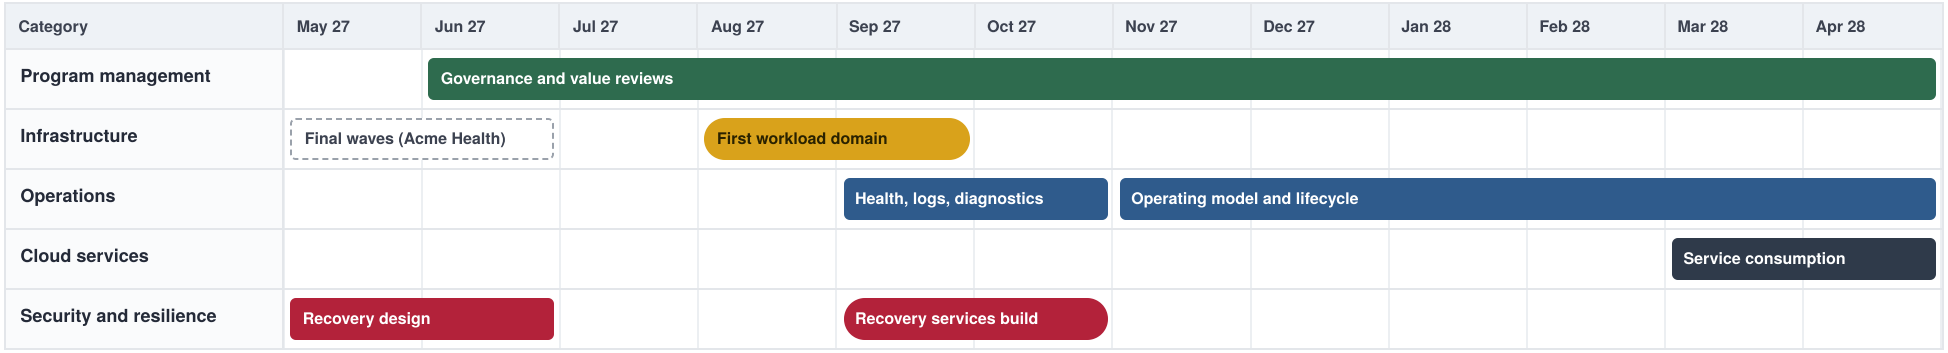

FOLLOW-ON WORK

PACKAGE	MONTH	HOURS
Recovery and resilience design	May 2027	10
First workload domain	Aug 2027	46
Health, logs and diagnostics	Sep 2027	30
Recovery services build	Sep 2027	31
Total follow-on		**117**

Estimated CDW hours, planned against a design already completed in year one.

HOW IT'S FUNDED

This work is **not drawn from the current entitlement**, which ends 28 April 2027.

It needs one of: a renewal with a services entitlement attached, a services purchase, or Broadcom Software Adoption Services hours.

The sooner it's funded, the sooner recovery protection is in place for the 330 VMs that are recovered by hand today.

Make Amazing Happen.

CDW · Proprietary and confidential. Copying restricted.
