FUNCTIONAL CONSUMPTION PLAN · ACME HEALTH

Amazing happens when Acme Health runs a modern VMware Cloud Foundation private cloud with confidence.

Make Amazing Happen.

PREPARED FOR
Acme Health

VERSION
1 · Issued 30 Sep 2026

PREPARED BY
CDW Consulting Solution Architecture

CDW · Proprietary and confidential. Copying restricted.

VMware Cloud Foundation Adoption: Acme Health

A design-led plan to move Acme Health onto VCF 9.1 on new hardware, consuming the services entitlement before it ends on 28 April 2027.

Platform: **VCF 9.1** · Path: **Greenfield with staging hardware** · Delivery: **CDW + Broadcom** · Segment: **Corporate** · Location: **Reno, NV**

$79,403	223 hrs	210 days	7.4 hrs/wk
VCF Services Entitlement	**Hours Remaining**	**Days to Expiry**	**Required Weekly Pace**
262 hours · 29 Apr 2026 to 28 Apr 2027	39 of 262 delivered as of 3 Sep 2026	Entitlement ends 28 Apr 2027	To consume by expiry · about 0.19 FTE

VERSION	SUPERSEDES	BROADCOM APPROVAL	CUSTOMER APPROVAL	REVISION
1, issued 30 Sep 2026	None	Pending	Pending	Initial plan, built from the VCF 9.1 assessment and the scoping questionnaire of 30 Sep 2026.

SUMMARY

CDW designs and builds a new VCF 9.1 foundation for Acme Health on new hardware, proves the migration runbook on the first waves, and hands the platform and the runbook to Acme Health's team, who run the remaining waves. VCF Operations becomes the team's daily view of health and capacity. Recovery design and the first workload domain follow after the entitlement.

SITUATION

- A DR site is being built: 8 new hosts and a NetApp array fed by SnapMirror. Recovery time objective and orchestration are not yet defined.
- Recovery of 330 powered-on VMs is manual today.
- The team wants to "make our lives easier" and use features it has already paid for.

PLAN ON A PAGE

- **Program management:** kickoff and delivery plan, hardware compatibility review. Assessment and discovery are already delivered.
- **Infrastructure:** design and bill of materials, VCF foundation build, migration plan, proving waves.
- **Operations:** VCF Operations design, role and access mapping, licensing, training, handover, runbook transfer.
- **Cloud services:** not requested (Kubernetes, Private AI, HCX).
- **Security and resilience:** recovery design and build, after the entitlement.

CDW · Proprietary and confidential. Copying restricted.

Scope and Architecture

What this plan delivers, what it doesn't, and the platform it builds.

IN SCOPE

Program management	Kickoff and delivery plan, hardware compatibility review against VCF 9.1 (assessment and discovery already delivered)
Infrastructure	Greenfield design and bill of materials, VCF foundation build, migration and cutover plan, proving migration waves
Operations	VCF Operations design and licensing, role and access mapping, training, runbook transfer, handover and service acceptance

OUT OF SCOPE

Cloud services	Kubernetes, Private AI and HCX were not requested.
Security and resilience	Recovery design and recovery services build follow after the entitlement (Roadmap, page 6).
Remaining migration waves	Run by Acme Health with the proven runbook.
First workload domain	Follows after the entitlement.

WHAT WE HEARD, AND WHERE IT LANDS

TOPIC	ACME HEALTH POSITION	WHERE IT LANDS
Goal	"Make our lives easier"; use features already paid for	VCF Operations enablement and a runbook the team repeats
Storage	Keep the existing array	Fibre Channel stays principal storage
Recovery	Manual recovery of 330 VMs today	Recovery design picks orchestration so DR runs under pressure

VCF DESIGN PROFILE

Consumption	VCF 9.1 with VCF Operations as the daily front door; vCenter consumption unchanged for the team; automation evaluated later.
Physical site	Primary data center and a new DR site.
Availability	Converged management domain on the primary cluster; HA and fully automated DRS retained.
Isolation	NSX deployed with VCF, VLAN-backed at first; no network redesign on day one.
Recoverability	DR site as a separate workload domain in the same fleet; orchestration tool chosen in the recovery design.
Expansion	Evacuated hosts rebuilt into VCF wave by wave; the DR workload domain added once the site is online.

PLATFORM FACTS

Hardware	Cisco UCS hosts; vLCM images with the Cisco vendor add-on
Storage	VMFS on Fibre Channel, existing NetApp array; no vSAN needed
Network	vDS, VLAN-backed today
Today	vSphere 8.0.3, 1 vCenter, 2 data centers

CDW · Proprietary and confidential. Copying restricted.

Work Packages and Scoped Effort

Each package with its window, lead role, CDW hours and how it is accepted. 39 hours delivered plus 223 planned equals the 262-hour entitlement. Estimated from this plan; the signed resource assignments replace these figures.

WORK PACKAGE	WINDOW	LEAD ROLE	ARCHITECT	SR. CONSULTANT	PM	TOTAL
DELIVERED TO DATE						
Assessment and discovery *Environment, DR site and priorities reviewed; VCF 9.1 assessment.*	*Jul to Sep 2026*	*VCF Architect*	*30*	*3*	*6*	*39*
PROGRAM MANAGEMENT						
Hardware compatibility review Every host model, CPU, adapter and ESX build checked against VCF 9.1 with the customer platform lead.	Oct 2026	VCF Architect	12	1	2	15
Kickoff and delivery plan Confirm design decisions, evidence, dependencies and delivery ownership.	Oct 2026	Project Manager	0	0	2	2
INFRASTRUCTURE						
Design and bill of materials Host and cluster sizing, storage, network, IP/DNS/NTP and the bill of materials. **Accepted when** architecture, network, storage and procurement owners approve.	Nov 2026	VCF Implementation Engineer	20	2	2	24
Migration and cutover plan Waves, dependencies, change windows, rollback and validation. **Accepted when** application and change owners approve wave assignments.	Dec 2026	Migration Lead	20	2	2	24
VCF foundation build Deploy the management domain and validate platform health. NSX VLAN-backed; overlay later. **Starts after** hardware sign-off.	Jan 2027	VCF Implementation Engineer	8	45	8	61
Proving migration waves CDW runs the first waves with the team shadowing, then reverse-shadowing. **Accepted when** each wave meets application and platform acceptance.	Mar to Apr 2027	Migration Lead	4	31	6	41
OPERATIONS						
VCF Operations design Architecture, data sources, dashboard and alert scope, lifecycle ownership.	Nov 2026	VCF Architect + Ops Lead	1	8	2	11
Role and access mapping Directory groups to vCenter, VCF Operations and SSO roles; least privilege and break-glass.	Dec 2026	VCF Architect	12	1	2	15
Training and knowledge transfer The team installs and runs the management domain alongside CDW.	Jan 2027	VCF Architect + Ops Lead	0	5	1	6
VCF Operations licensing Activate subscription licensing before the evaluation period ends.	Feb 2027	VCF Architect + Ops Lead	1	5	1	7
Handover and service acceptance Confirm the operating model, evidence, ownership and lifecycle cadence.	Apr 2027	VCF Architect + Ops Lead	1	9	1	11
Runbook knowledge transfer Hand over the proven migration runbook so the team runs the later waves.	Apr 2027	VCF Architect + Ops Lead	0	5	1	6
Total, funded by the entitlement			**109**	**117**	**36**	**262**

CDW · Proprietary and confidential. Copying restricted.

Adoption Timeline

1 October 2026 through 28 April 2027, the entitlement window. Dashed bars are run by Acme Health. Rounded bars mark key delivered functionality.

Governance · Infrastructure build · Migration · Operations · Run by Acme Health

Category	Oct 26	Nov 26	Dec 26	Jan 27	Feb 27	Mar 27	Apr 27
Program management	Kickoff and delivery plan Hardware sign-off						
Infrastructure	Close HCL evidence gaps	Design and BOM	Migration plan	VCF foundation build	Acme Health migration waves and legacy cluster retirement	Proving migration waves	
Operations		VCF Ops design	Role and access	Training	Licensing		Handover Runbook transfer
Cloud services	*Not in this plan*						
Security and resilience	*Recovery design and build follow after the entitlement (Roadmap, page 6)*						

MILESTONES TO DATE

29 Apr 2026	Entitlement effective; 262-hour services entitlement opened
21 Jul 2026	Discovery session: environment, DR site and priorities reviewed
30 Sep 2026	Functional Consumption Plan version 1 issued

KEY DATES


1 Oct 2026	Design and planning start
30 Nov 2026	Acme Health decisions due: build hosts, DR direction, wave ownership
1 Jan 2027	Platform build begins
Mar 2027	First proving wave
28 Apr 2027	Entitlement ends; unused hours are not refunded

CDW · Proprietary and confidential. Copying restricted.

Roadmap: After the Entitlement

May 2027 through April 2028. Directional work that is not funded by the current entitlement and needs a renewal with entitlement attached or a services purchase.

Governance · Infrastructure build · Operations · Consume and handover · Security and resilience · Run by Acme Health

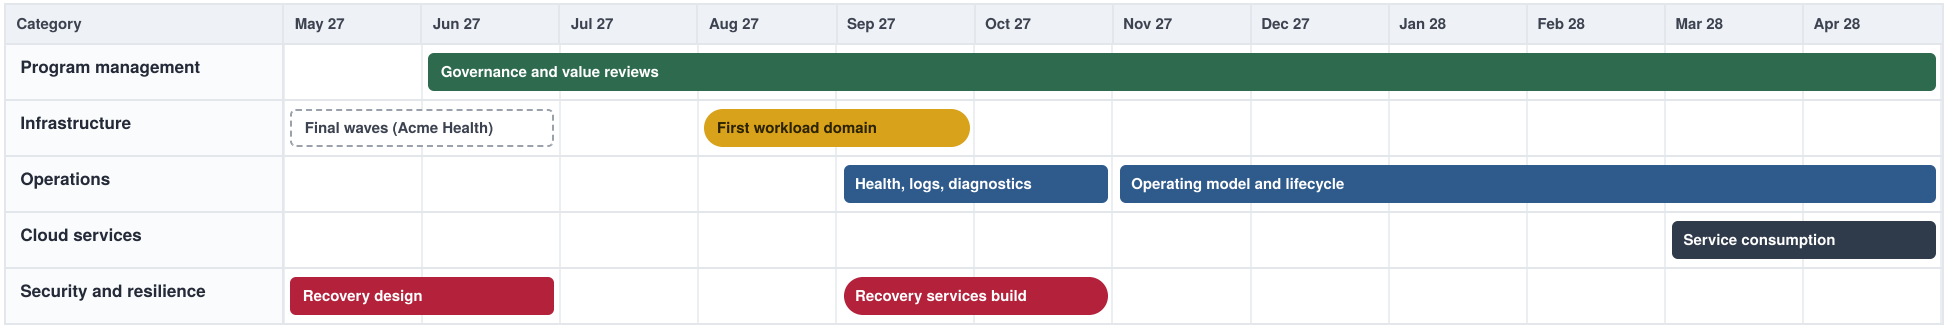

FOLLOW-ON SCOPE

WORK PACKAGE	PLANNED WINDOW	LEAD ROLE	ARCHITECT	SR. CONSULTANT	PM	TOTAL HOURS
Recovery and resilience design	May 2027	Security / Resilience Engineer	1	8	1	10
First workload domain	Aug 2027	VCF Implementation Engineer	4	36	6	46
Health, logs and diagnostics	Sep 2027	VCF Architect + Ops Lead	2	24	4	30
Recovery services build	Sep 2027	Security / Resilience Engineer	2	25	4	31
Total follow-on hours			**9**	**93**	**15**	**117**

Working Together

What Acme Health's team commits to, what shapes the sequence, and who is involved.

ACME HEALTH TEAM EFFORT

PHASE	WINDOW	HRS / WEEK	FTE
Design sessions and sign-off	Oct to Dec 2026	7	0.18
Platform build	Oct 2026 to Jan 2027	8	0.20
Capability enablement	Feb 2027	7	0.18
Acme Health migration waves	Feb to Apr 2027	30	0.75
Knowledge transfer and handover	Apr 2027	6	0.15

COMMITMENTS

- **Inventory:** a current RVTools export before the first design session.
- **People:** platform, network and operations leads available for design sessions.
- **Migration:** Acme Health runs the waves after the proving waves, using the runbook.

DECISIONS NEEDED

DECISION	NEEDED BY	OWNER
Hosts for the build	30 Nov 2026	Pat Rivera
DR policy direction	30 Nov 2026	Pat Rivera
Wave ownership	30 Nov 2026	Pat Rivera

SEQUENCING CONSTRAINTS

CONSTRAINT	EFFECT ON THE SEQUENCE
Design and a current inventory before the build	Build starts after design sign-off
Management domain before any workload moves	Proving waves follow the build
DR site online before DR build and testing	Recovery design now; build follows the site
Entitlement ends 28 Apr 2027	Handover completes in April 2027

OPEN ITEMS

ITEM	WHAT IT GATES	OWNER
Current RVTools export	Design sign-off and sizing	Pat Rivera

WHO IS INVOLVED

NAME	ROLE	ORGANIZATION
Pat Rivera	Platform lead	Acme Health
Sam Lee	Network	Acme Health
Jordan Blake	Architect	CDW
Casey Morgan	Sr. Consultant	CDW
Alex Kim	Project Manager	Broadcom

Make Amazing Happen.

CDW · Proprietary and confidential. Copying restricted.
