FUNCTIONAL CONSUMPTION PLAN · STANDARD

VMware vSphere Foundation Adoption: Cedar Ridge Logistics

Amazing happens when Cedar Ridge Logistics runs a modern VVF 9.1 private cloud with confidence.

Prepared for Cedar Ridge Logistics

Version 1 · Issued 30 Sep 2026

Prepared by CDW Consulting Solution Architecture

Make Amazing Happen.

CDW · Proprietary and confidential. Copying restricted.

VMware vSphere Foundation Adoption: Cedar Ridge Logistics

Platform: **VVF 9.1** · Path: **Greenfield VVF with staging hardware** · Delivery: **CDW** · Location: **Duluth, MN**

318 hrs	2 Nov 2026	31 Jul 2027	Not yet booked
Planned CDW Hours	**Plan Starts**	**Planned Completion**	**Entitlement**
Estimated from this plan	Design and planning first; build from 1 Feb 2027	Estimated from this plan	Hours and term to be confirmed

VERSION	SUPERSEDES	REVISION
1, issued 30 Sep 2026	None	Initial plan

SUMMARY

CDW designs and builds the VVF 9.1 foundation for Cedar Ridge Logistics, proves the runbook and hands the platform over, and Cedar Ridge Logistics's team repeats it. The plan is framed around operations and lifecycle management, with a separately funded greenfield VVF foundation and workload migration path on VMware vSphere Foundation (VVF).

SITUATION

- 8 ESXi hosts · 120 VMs and 1 cluster

PLAN ON A PAGE

IN THIS PLAN

- **Program Management & Governance:** Greenfield Discovery Sessions and Funding, Hardware Compatibility Review, Kickoff and Delivery Plan
- **Modernize Infrastructure:** Reference Architecture Design, Greenfield VVF Foundation Build, Workload Clusters and vLCM Images, Workload Migration and Cutover
- **Operations:** VCF Operations Design, Role and Access Mapping, Training and Knowledge Transfer, VCF Operations Licensing, Platform Lifecycle and Service Health, Runbook Knowledge Transfer, Handover and Service Acceptance

NOT IN THIS PLAN

- **Modernize Cloud:** not in this plan
- **Modernize Security & Resilience:** not in this plan
- **Run by Cedar Ridge Logistics:** Site prerequisites and hardware evidence; Remaining migration waves, run by Cedar Ridge Logistics with the proven runbook

CDW · Proprietary and confidential. Copying restricted.

Scope and Architecture

What this plan delivers, what it doesn't, and the platform it builds.

IN THIS PLAN

- **Program Management & Governance:** Greenfield Discovery Sessions and Funding, Hardware Compatibility Review, Kickoff and Delivery Plan
- **Modernize Infrastructure:** Reference Architecture Design, Greenfield VVF Foundation Build, Workload Clusters and vLCM Images, Workload Migration and Cutover
- **Operations:** VCF Operations Design, Role and Access Mapping, Training and Knowledge Transfer, VCF Operations Licensing, Platform Lifecycle and Service Health, Runbook Knowledge Transfer, Handover and Service Acceptance

NOT IN THIS PLAN

- **Modernize Cloud:** not in this plan
- **Modernize Security & Resilience:** not in this plan
- **Run by Cedar Ridge Logistics:** Site prerequisites and hardware evidence; Remaining migration waves, run by Cedar Ridge Logistics with the proven runbook

VVF DESIGN PROFILE

AREA	DESIGN
Consumption	VVF 9.1 with VCF Operations as the daily operations console; automation evaluated later.
Physical site	1 site, 8 hosts in the current estate.
Availability	Management domain topology to be decided in design.
Isolation	vSphere Distributed Switch networking; no NSX overlay in VVF.
Recoverability	Recovery approach to be confirmed in design.
Expansion	Capacity added wave by wave as hosts are evacuated and rebuilt into the platform.

CDW · Proprietary and confidential. Copying restricted.

Work Packages and Scoped Effort


Each package with its window, lead role, CDW hours and how it is accepted. CDW-delivered hours. The signed resource assignments replace these estimates.

WORK PACKAGE	WINDOW	LEAD ROLE	ARCHITECT	SR. CONSULTANT	PM	TOTAL
PROGRAM MANAGEMENT & GOVERNANCE						
Greenfield Discovery Sessions and Funding Run the design discovery sessions to confirm separately funded hardware, capacity, vSAN capacity entitlement, site constraints, workload scope, and acceptance boundaries. Accepted when: Funding owner confirms hardware and non-service dependencies.	Nov 2026	Senior Consultant	11	31	5	47
Hardware Compatibility Review CDW's architect reviews every host model, CPU, adapter and ESX build against the target release with the customer platform lead, and records each as listed, to confirm, or replace.	Nov 2026	VCF Architect with the customer platform lead	10	1	1	12
Kickoff and Delivery Plan Use the opening window to confirm design decisions, evidence, dependencies, and delivery ownership; implementation services begin only in the selected implementation window.	Nov 2026	Engagement Manager / Project Manager	0	0	2	2
MODERNIZE INFRASTRUCTURE						
Reference Architecture Design In design sessions, design the platform: host and cluster sizing, storage, VDS networking, IP/DNS/NTP, and the bill of materials. Accepted when: Architecture, infrastructure, network, storage, and procurement owners approve the design.	Dec 2026	VCF Implementation Engineer	20	2	3	25
Greenfield VVF Foundation Build Deploy vCenter, VCF Operations, and management services with the VCF Installer and validate core platform health.	Feb 2027	VCF Implementation Engineer	3	33	5	41
Workload Clusters and vLCM Images Prepare the workload clusters used by migration waves and selected component adoption.	Mar 2027	VCF Implementation Engineer	1	13	2	16
Workload Migration and Cutover Move the approved workloads, wave by wave, to the accepted VVF foundation and validate service restoration. Accepted when: Each wave meets application, platform, and operational acceptance criteria.	Apr – Jun 2027	Migration Lead + Application Owners	9	92	15	116
OPERATIONS						
VCF Operations Design In design sessions, design the Operations architecture, data sources, dashboard and alert scope, lifecycle ownership, and operating acceptance criteria.	Dec 2026	VCF Architect + Operations Lead	1	5	1	7
Role and Access Mapping In design sessions, map the directory groups to vCenter, VCF Operations and SSO roles, with least-privilege service accounts and break-glass access.	Jan 2027	VCF Architect with the customer identity owner	10	1	1	12
Training and Knowledge Transfer Hands-on enablement: the platform team installs and operates the management domain alongside CDW, covering deployment, lifecycle and VCF Operations, so it learns by doing from the first build.	Feb 2027	VCF Architect + Operations Lead	0	3	1	4
VCF Operations Licensing Activate subscription licensing for the deployed platform and its add-ons before the evaluation period ends.	Mar 2027	VCF Architect + Operations Lead	0	3	1	4
Platform Lifecycle and Service Health Implement the selected operating capability with accountable ownership and measurable service outcomes.	Apr 2027	VCF Architect + Operations Lead	2	15	2	19
Runbook Knowledge Transfer Hand over the proven migration runbook with shadowed then reverse-shadowed waves, so the team runs the later waves itself.	Jun 2027	VCF Architect + Operations Lead	0	3	1	4
Handover and Service Acceptance Confirm the operating model, evidence, ownership, and the continuing lifecycle cadence.	Jul 2027	VCF Architect + Operations Lead	1	7	1	9
Total CDW hours			**68**	**209**	**41**	**318**

Adoption Timeline

2 November 2026 through 31 July 2027, the planned delivery window. Dashed bars are run by Cedar Ridge Logistics. ◆ marks key delivered functionality.

DELIVERY WORKSTREAM KEY: Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Customer-owned · ◆ Checkpoint

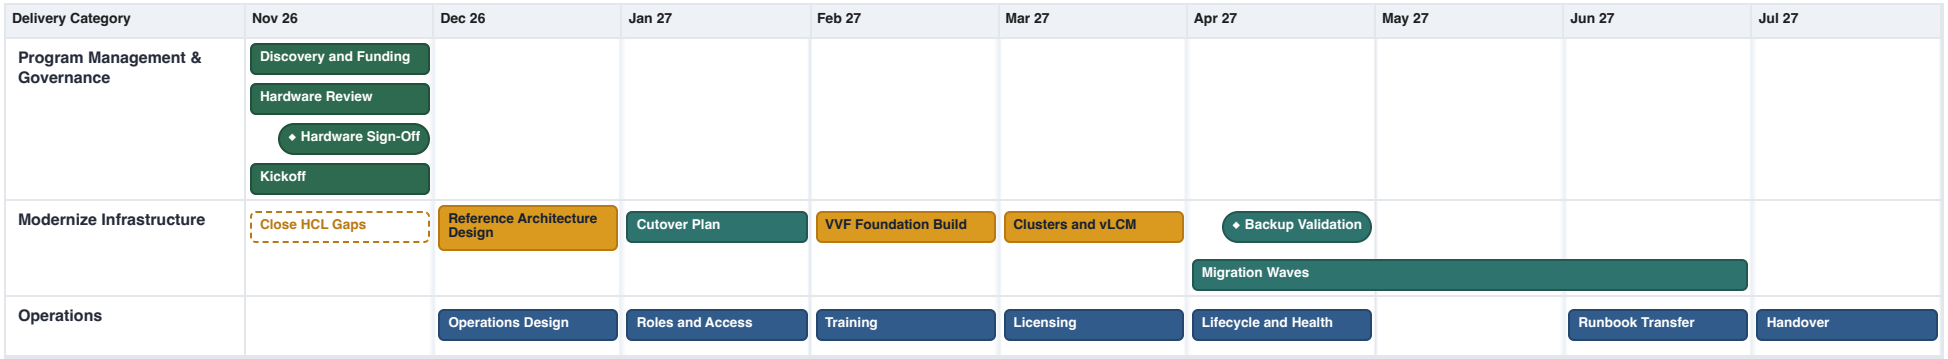

KEY DATES

2 Nov 2026	Design and planning start
1 Feb 2027	Platform build begins
31 Jul 2027	Planned completion

Working Together

What Cedar Ridge Logistics's team commits to, what shapes the sequence, and who is involved.

CEDAR RIDGE LOGISTICS TEAM EFFORT

PHASE	WINDOW	HRS / WEEK	FTE
Platform build	Nov 2026 – Mar 2027	8	0.2
Design sessions and design sign-off	Nov 2026 – Jan 2027	7	0.18
Capability enablement	Mar – Apr 2027	7	0.18
Migration waves	Apr – Jun 2027	15	0.38
Knowledge transfer and handover	Jul 2027	6	0.15
Customer-run migration waves	Jul – Sep 2027	30	0.75

COMMITMENTS

- **Effort:** 6–30 hours per week, peaking at 0.75 FTE during customer-run migration waves

WORK RUN BY CEDAR RIDGE LOGISTICS

WORK	WINDOW
Site prerequisites and hardware evidence	Nov 2026
Remaining migration waves, run by Cedar Ridge Logistics with the proven runbook	Jul – Sep 2027

SEQUENCING CONSTRAINTS

CONSTRAINT	EFFECT ON THE SEQUENCE
Design and a current inventory before the build	Build starts after design sign-off
Management domain before any workload moves	Proving wave follows the build
Implementation services start 2 Nov 2026 with design and planning; the platform build begins 1 Feb 2027	Design and planning run from the project start; build, upgrade and migration begin with the platform build

ACCEPTANCE

CEDAR RIDGE LOGISTICS

NAME

TITLE

DATE

SIGNATURE

Make Amazing Happen.
