FUNCTIONAL CONSUMPTION PLAN · SUMMARY

VMware Cloud Foundation Adoption: Acme Health

Version 1
Issued 30 Sep 2026
Prepared by CDW Consulting Solution Architecture

Platform: **VCF 9.1** · Path: **Greenfield with staging hardware** · Delivery: **CDW + Broadcom** · Location: **Reno, NV**

$79,403	223 hrs	1 Oct 2026	28 Apr 2027
VCF Services Entitlement	**Hours Remaining**	**Plan Starts**	**Entitlement Ends**
262 hours · 29 Apr 2026 to 28 Apr 2027	39 of 262 delivered as of 3 Sep 2026	Design and planning first; build from 1 Jan 2027	Unused hours are not refunded

WHAT WE'RE DOING

CDW designs and builds the VCF 9.1 foundation for Acme Health, runs the migration waves and hands the platform over. The plan is framed around operations and lifecycle management and resilience and recovery planning, with a separately funded greenfield VCF foundation and workload migration path.

IN THIS PLAN

- **Program Management & Governance:** Hardware Compatibility Review, Kickoff and Delivery Plan
- **Modernize Infrastructure:** Reference Architecture Design, Migration and Cutover Plan, Greenfield VCF Foundation Build
- **Operations:** VCF Operations Design, Optimization and Advisory Services, Role and Access Mapping, Training and Knowledge Transfer, VCF Operations Licensing, Handover and Service Acceptance
- **Modernize Security & Resilience:** Recovery and Resilience Design

NOT IN THIS PLAN

- **Modernize Infrastructure:** First Workload Domain, Workload Migration and Cutover, after the entitlement
- **Operations:** Health, Logs, and Diagnostics, after the entitlement
- **Modernize Cloud:** not requested (Kubernetes, Private AI and HCX)
- **Modernize Security & Resilience:** Recovery Services Build, after the entitlement
- **Run by Acme Health:** Site prerequisites and hardware evidence; Legacy cluster retirement

ARCHITECTURE AT A GLANCE

Platform	VCF 9.1 on Cisco UCS hosts. Converged management domain: management components and production workloads share the primary cluster. Primary data center and a new DR site.
Storage, network	Fibre Channel. NSX deployed with VCF, VLAN-backed at first.
Recovery	DR site as a separate workload domain in the same fleet.

WORK PACKAGES

PACKAGE	MONTH	HOURS
DELIVERED TO DATE		
Hours delivered to date	*Apr – Sep 2026*	*39*
PROGRAM MANAGEMENT & GOVERNANCE		
Hardware Compatibility Review	Oct 2026	13
Kickoff and Delivery Plan	Oct 2026	2
MODERNIZE INFRASTRUCTURE		
Reference Architecture Design	Nov 2026	40
Migration and Cutover Plan	Dec 2026	24
Greenfield VCF Foundation Build	Jan 2027	63
OPERATIONS		
VCF Operations Design	Nov 2026	10
Optimization and Advisory Services	Dec 2026 – Apr 2027	5
Role and Access Mapping	Dec 2026	13
Training and Knowledge Transfer	Jan 2027	7
VCF Operations Licensing	Feb 2027	7
Handover and Service Acceptance	Apr 2027	11
MODERNIZE SECURITY & RESILIENCE		
Recovery and Resilience Design	Nov 2026	10
Held for change requests, released to follow-on work if unused		18
Total, funded by the entitlement		**262**


CDW-delivered hours: 39 delivered, 205 planned and 18 held for change requests add up to the 262-hour entitlement. The signed resource assignments replace these estimates.

CDW · Proprietary and confidential. Copying restricted.

Timeline

1 October 2026 through 28 April 2027, the entitlement window. Dashed bars are run by Acme Health. ◆ marks key delivered functionality.

DELIVERY WORKSTREAM KEY: Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Consume / Handover · Security & Resiliency · Customer-owned · ◆ Checkpoint

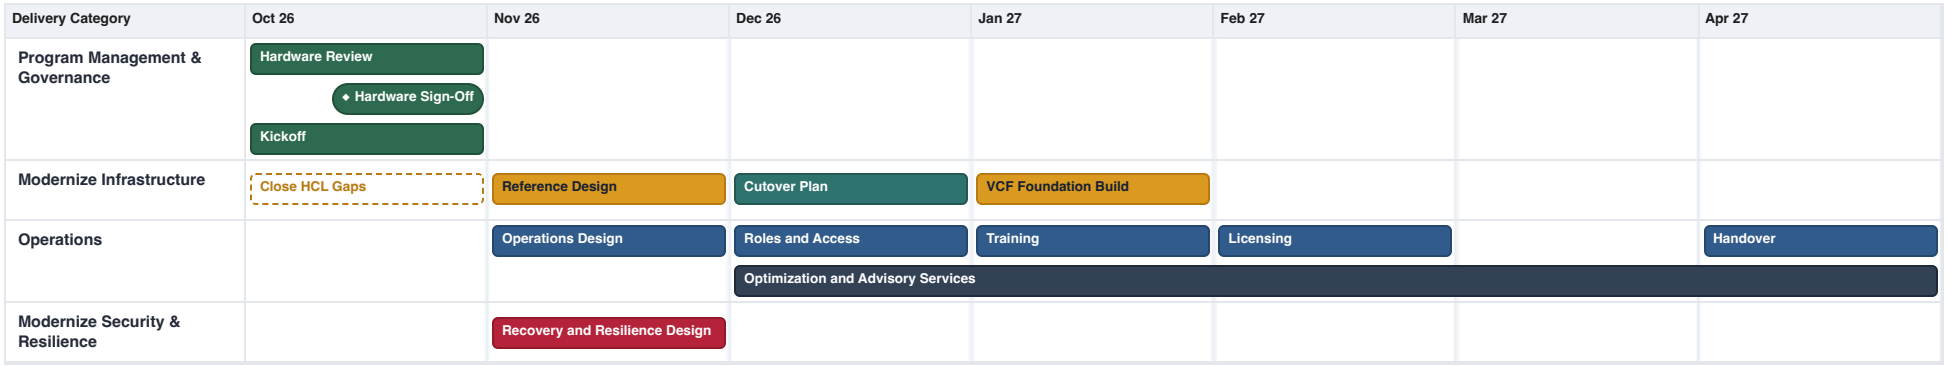

KEY DATES

1 Oct 2026	Design and planning start
1 Jan 2027	Platform build begins
28 Apr 2027	Entitlement ends; unused hours are not refunded

WHAT WE NEED FROM ACME HEALTH

- **Effort:** 6–8 hours per week, peaking at 0.2 FTE during platform build
- **Decisions by November:** hosts for the build, DR policy direction, wave ownership

OPEN ITEMS

Current RVTools export	Design sign-off and sizing	Pat Rivera


AFTER THIS PLAN

> About **315 hours** of follow-on work runs from May 2027. The two-year view and how it's funded are on page 3.

After the Entitlement

May 2027 through Apr 2028, the second year of the two-year view. This is where Acme Health goes next. None of it is funded by the current entitlement.

DELIVERY WORKSTREAM KEY — Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Consume / Handover · Security & Resiliency · ◆ Checkpoint

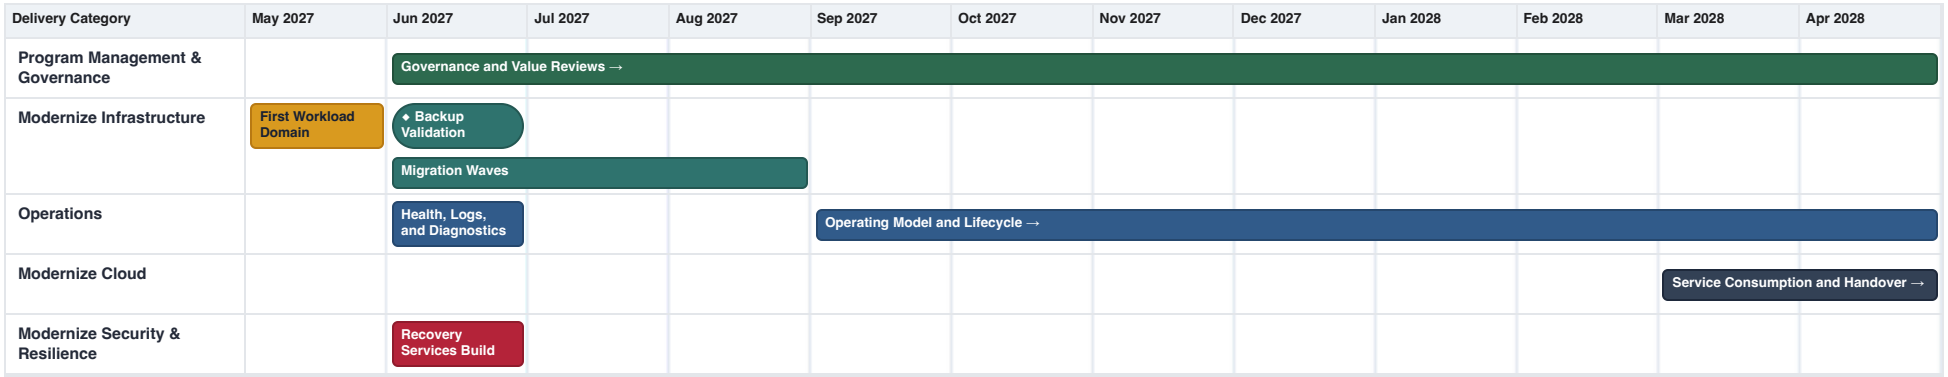

FOLLOW-ON WORK

PACKAGE	MONTH	HOURS
First Workload Domain Create the workload-domain foundation used by migration waves and selected component adoption.	May 2027	39
Workload Migration and Cutover Move the approved workloads, wave by wave, to the accepted VCF foundation and validate service restoration. Accepted when: Each wave meets application, platform, and operational acceptance criteria.	Jun – Aug 2027	215
Health, Logs, and Diagnostics Implement the selected operating capability with accountable ownership and measurable service outcomes.	Jun 2027	30
Recovery Services Build Implement the selected resilience and security capability with controlled evidence and ownership.	Jun 2027	31
Total follow-on		**315**

Estimated CDW hours, planned against a design already completed in year one.

HOW IT'S FUNDED

> This work is not drawn from the current entitlement, which ends 28 April 2027.
>
> It needs one of: a renewal with a services entitlement attached, a services purchase, or Broadcom Software Adoption Services hours.

Make Amazing Happen.
