FUNCTIONAL CONSUMPTION PLAN · STANDARD

VMware Cloud Foundation Adoption: Acme Health

Amazing happens when Acme Health runs a modern VCF 9.1 private cloud with confidence.

Prepared for Acme Health

Version 1 · Issued 30 Sep 2026

Prepared by CDW Consulting Solution Architecture

Make Amazing Happen.

VMware Cloud Foundation Adoption: Acme Health

Platform: **VCF 9.1** · Path: **Greenfield with staging hardware** · Delivery: **CDW + Broadcom** · Location: **Reno, NV**

$79,403	223 hrs	1 Oct 2026	28 Apr 2027
VCF Services Entitlement	**Hours Remaining**	**Plan Starts**	**Entitlement Ends**
262 hours · 29 Apr 2026 to 28 Apr 2027	39 of 262 delivered as of 3 Sep 2026	Design and planning first; build from 1 Jan 2027	Unused hours are not refunded

VERSION	SUPERSEDES	REVISION
1, issued 30 Sep 2026	None	Built from the VCF 9.1 assessment and the scoping questionnaire of 30 Sep 2026.

SUMMARY

CDW designs and builds the VCF 9.1 foundation for Acme Health, proves the runbook and hands the platform over. The plan is framed around operations and lifecycle management and resilience and recovery planning, with a separately funded greenfield VCF foundation and workload migration path.

SITUATION

- 14 ESXi hosts across 1 vCenter and 1 cluster
- DR site being built: 8 new hosts and a NetApp array fed by SnapMirror; recovery time objective and orchestration not yet defined

PLAN ON A PAGE

IN THIS PLAN

- **Program Management & Governance:** Hardware Compatibility Review, Kickoff and Delivery Plan
- **Modernize Infrastructure:** Reference Architecture Design, Migration and Cutover Plan, Greenfield VCF Foundation Build
- **Operations:** VCF Operations Design, Optimization and Advisory Services, Role and Access Mapping, Training and Knowledge Transfer, VCF Operations Licensing, Handover and Service Acceptance
- **Modernize Security & Resilience:** Recovery and Resilience Design

NOT IN THIS PLAN

- **Modernize Infrastructure:** First Workload Domain, Workload Migration and Cutover, after the entitlement
- **Operations:** Health, Logs, and Diagnostics, Runbook Knowledge Transfer, after the entitlement
- **Modernize Cloud:** not requested (Kubernetes, Private AI and HCX)
- **Modernize Security & Resilience:** Recovery Services Build, after the entitlement
- **Run by Acme Health:** Site prerequisites and hardware evidence; Customer migration waves and legacy cluster retirement

CDW · Proprietary and confidential. Copying restricted.

Scope and Architecture

What this plan delivers, what it doesn't, and the platform it builds.

IN THIS PLAN

- **Program Management & Governance:** Hardware Compatibility Review, Kickoff and Delivery Plan
- **Modernize Infrastructure:** Reference Architecture Design, Migration and Cutover Plan, Greenfield VCF Foundation Build
- **Operations:** VCF Operations Design, Optimization and Advisory Services, Role and Access Mapping, Training and Knowledge Transfer, VCF Operations Licensing, Handover and Service Acceptance
- **Modernize Security & Resilience:** Recovery and Resilience Design

NOT IN THIS PLAN

- **Modernize Infrastructure:** First Workload Domain, Workload Migration and Cutover, after the entitlement
- **Operations:** Health, Logs, and Diagnostics, Runbook Knowledge Transfer, after the entitlement
- **Modernize Cloud:** not requested (Kubernetes, Private AI and HCX)
- **Modernize Security & Resilience:** Recovery Services Build, after the entitlement
- **Run by Acme Health:** Site prerequisites and hardware evidence; Customer migration waves and legacy cluster retirement

WHAT WE HEARD, AND WHERE IT LANDS

TOPIC	ACME HEALTH POSITION	WHERE IT LANDS
Goal	"Make our lives easier"; use features already paid for	Operations and logs enablement; a runbook the team repeats
Storage	Keep the existing array	Fibre Channel stays principal storage

VCF DESIGN PROFILE

AREA	DESIGN
Consumption	VCF 9.1 with VCF Operations as the daily front door; vCenter consumption unchanged for the team; automation evaluated later.
Physical site	Primary data center and a new DR site.
Availability	Converged management domain: management components and production workloads share the primary cluster; HA and fully automated DRS retained.
Isolation	NSX deployed with VCF, VLAN-backed at first; no network redesign on day one.
Recoverability	DR site as a separate workload domain in the same fleet; replication with an orchestration tool to be chosen.
Expansion	Evacuated hosts rebuilt into VCF wave by wave; the DR workload domain added once the site is online.

CDW · Proprietary and confidential. Copying restricted.

Work Packages and Scoped Effort


Each package with its window, lead role, CDW hours and how it is accepted. CDW-delivered hours: 39 delivered, 205 planned and 18 held for change requests add up to the 262-hour entitlement. The signed resource assignments replace these estimates.

WORK PACKAGE	WINDOW	LEAD ROLE	ARCHITECT	SR. CONSULTANT	PM	TOTAL
PROGRAM MANAGEMENT & GOVERNANCE						
Hardware Compatibility Review CDW's architect reviews every host model, CPU, adapter and ESX build against the target release with the customer platform lead, and records each as listed, to confirm, or replace.	Oct 2026	VCF Architect with the customer platform lead	10	1	2	13
Kickoff and Delivery Plan Use the opening window to confirm design decisions, evidence, dependencies, and delivery ownership; implementation services begin only in the selected implementation window.	Oct 2026	Engagement Manager / Project Manager	0	0	2	2
MODERNIZE INFRASTRUCTURE						
Reference Architecture Design In design sessions, design the platform: host and cluster sizing, storage, network, IP/DNS/NTP, and the bill of materials. Accepted when: Architecture, infrastructure, network, storage, and procurement owners approve the design.	Nov 2026	VCF Implementation Engineer	32	3	5	40
Migration and Cutover Plan In design sessions, group applications into migration waves and plan their dependencies, change windows, rollback, validation, and legacy decommissioning. Accepted when: Application and change owners approve wave assignments and acceptance criteria.	Dec 2026	Migration Lead + Application Owners	19	2	3	24
Greenfield VCF Foundation Build Deploy the approved management-domain foundation and validate core platform health.	Jan 2027	VCF Implementation Engineer	8	47	8	63
OPERATIONS						
VCF Operations Design In design sessions, design the Operations architecture, data sources, dashboard and alert scope, lifecycle ownership, and operating acceptance criteria.	Nov 2026	VCF Architect + Operations Lead	1	8	1	10
Optimization and Advisory Services Time-boxed architect and consultant hours drawn down on request through the end of the entitlement: health checks, tuning, configuration reviews, and advisory sessions on the delivered platform.	Dec 2026 – Apr 2027	VCF Architect with a Senior Consultant	2	3	1	6
Role and Access Mapping In design sessions, map the directory groups to vCenter, VCF Operations and SSO roles, with least-privilege service accounts and break-glass access.	Dec 2026	VCF Architect with the customer identity owner	10	1	2	13
Training and Knowledge Transfer Hands-on enablement: the platform team installs and operates the management domain alongside CDW, covering deployment, lifecycle and VCF Operations, so it learns by doing from the first build.	Jan 2027	VCF Architect + Operations Lead	1	4	1	6
VCF Operations Licensing Activate subscription licensing for the deployed platform and its add-ons before the evaluation period ends.	Feb 2027	VCF Architect + Operations Lead	1	5	1	7
Handover and Service Acceptance Confirm the operating model, evidence, ownership, and the continuing lifecycle cadence.	Apr 2027	VCF Architect + Operations Lead	1	9	1	11
MODERNIZE SECURITY & RESILIENCE						
Recovery and Resilience Design In design sessions, set protection tiers and RPO/RTO, design the recovery topology, and write the runbooks, exercise model, and acceptance evidence.	Nov 2026	Security / Resilience Engineer	1	8	1	10
Total planned			**86**	**91**	**28**	**205**
DELIVERED TO DATE						
Hours delivered to date	*Apr – Sep 2026*					*39*
Held for change requests, released to follow-on work if unused						18
Total, funded by the entitlement						**262**

Adoption Timeline

1 October 2026 through 28 April 2027, the entitlement window. Dashed bars are run by Acme Health. ◆ marks key delivered functionality.

DELIVERY WORKSTREAM KEY: Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Consume / Handover · Security & Resiliency · Customer-owned · ◆ Checkpoint

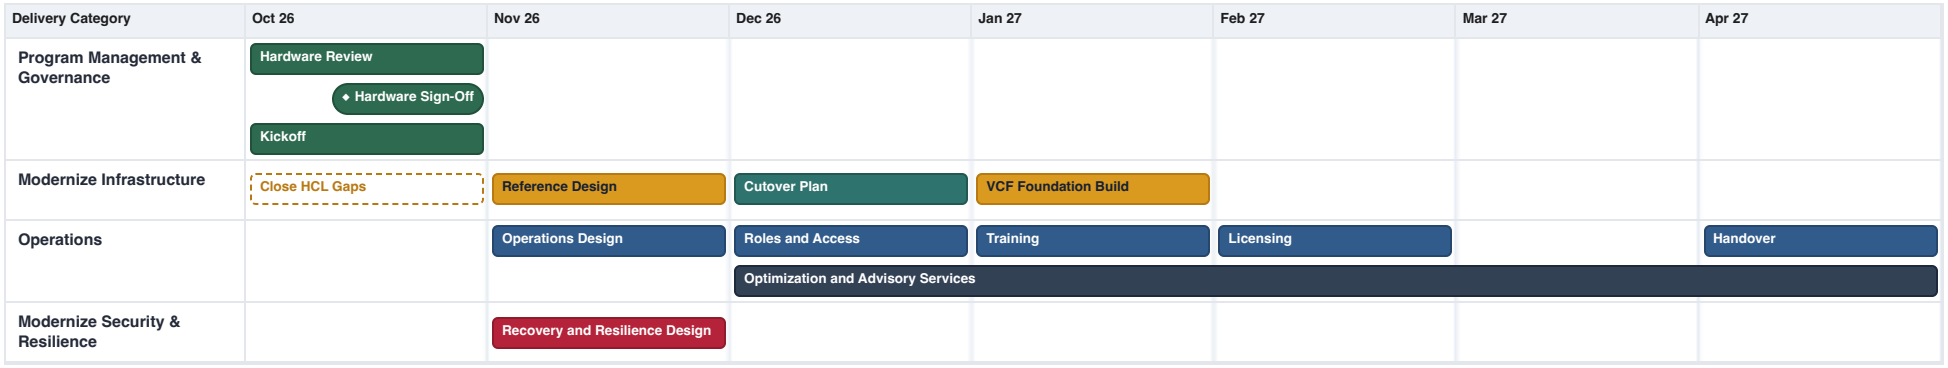

MILESTONES TO DATE

29 Apr 2026	Entitlement effective
21 Jul 2026	Discovery session

KEY DATES


1 Oct 2026	Design and planning start
1 Jan 2027	Platform build begins
28 Apr 2027	Entitlement ends; unused hours are not refunded

CDW · Proprietary and confidential. Copying restricted.

After the Entitlement

May 2027 through Apr 2028, the second year of the two-year view. This is where Acme Health goes next. None of it is funded by the current entitlement.

DELIVERY WORKSTREAM KEY: Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Consume / Handover · Security & Resiliency · ◆ Checkpoint

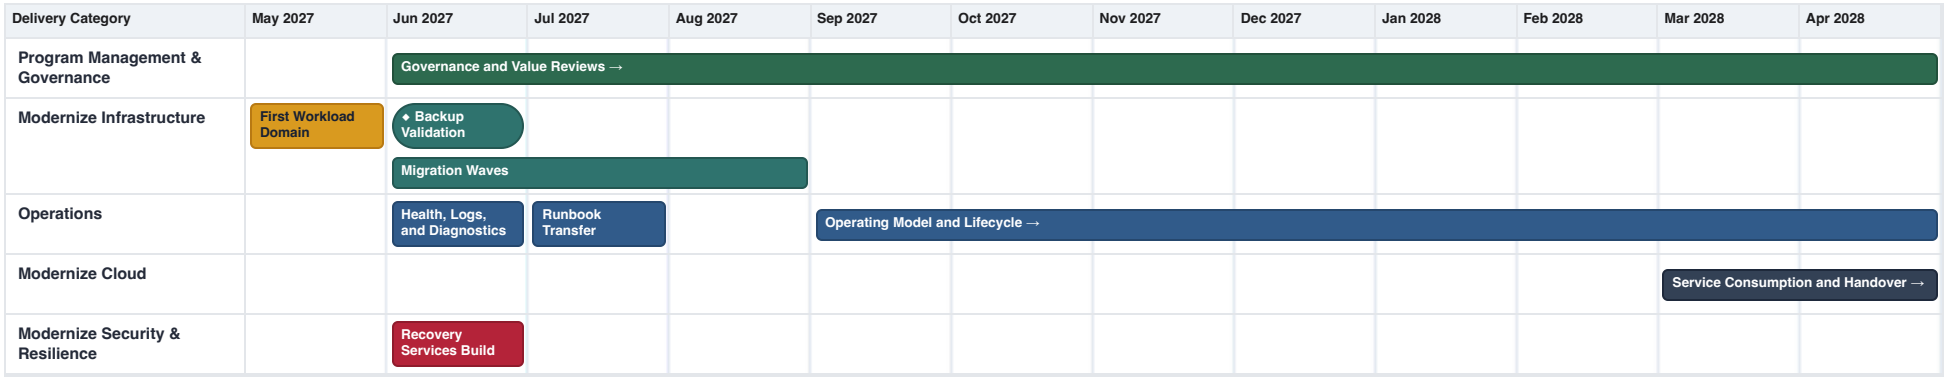

FOLLOW-ON WORK

WORK PACKAGE	PLANNED WINDOW	LEAD ROLE	ARCHITECT	SR. CONSULTANT	PM	TOTAL HOURS
First Workload Domain Create the workload-domain foundation used by migration waves and selected component adoption.	May 2027	VCF Implementation Engineer	3	33	5	41
Workload Migration and Cutover Move the approved workloads, wave by wave, to the accepted VCF foundation and validate service restoration. Accepted when: Each wave meets application, platform, and operational acceptance criteria.	Jun – Aug 2027	Migration Lead + Application Owners	17	170	28	215
Health, Logs, and Diagnostics Implement the selected operating capability with accountable ownership and measurable service outcomes.	Jun 2027	VCF Architect + Operations Lead	2	24	4	30

HOW IT'S FUNDED

> This work is not drawn from the current entitlement, which ends 28 April 2027.
>
> It needs one of: a renewal with a services entitlement attached, a services purchase, or Broadcom Software Adoption Services hours.

WORK PACKAGE	PLANNED WINDOW	LEAD ROLE	ARCHITECT	SR. CONSULTANT	PM	TOTAL HOURS
Runbook Knowledge Transfer Hand over the proven migration runbook with shadowed then reverse-shadowed waves, so the team runs the later waves itself.	Jul 2027	VCF Architect + Operations Lead	0	5	1	6
Recovery Services Build Implement the selected resilience and security capability with controlled evidence and ownership.	Jun 2027	Security / Resilience Engineer	2	25	4	31
Total follow-on hours			**24**	**257**	**42**	**323**

Estimated CDW hours, planned against a design already completed in year one.

Working Together

What Acme Health's team commits to, what shapes the sequence, and who is involved.

ACME HEALTH TEAM EFFORT

PHASE	WINDOW	HRS / WEEK	FTE
Design sessions and design sign-off	Oct – Dec 2026	7	0.18
Platform build	Oct 2026 – Jan 2027	8	0.2
Capability enablement	Feb 2027	7	0.18
Customer-run migration waves	Feb – Apr 2027	30	0.75
Knowledge transfer and handover	Apr 2027	6	0.15

COMMITMENTS

- **Effort:** 6–30 hours per week, peaking at 0.75 FTE during customer-run migration waves
- **Decisions by November:** hosts for the build, DR policy direction, wave ownership

WORK RUN BY ACME HEALTH

WORK	WINDOW
Site prerequisites and hardware evidence	Oct 2026
Customer migration waves and legacy cluster retirement	Feb – Apr 2027

SEQUENCING CONSTRAINTS

CONSTRAINT	EFFECT ON THE SEQUENCE
Design and a current inventory before the build	Build starts after design sign-off
Management domain before any workload moves	Proving wave follows the build
Implementation services start 1 Oct 2026 with design and planning; the platform build begins 1 Jan 2027	Design and planning run from the project start; build, upgrade and migration begin with the platform build
Entitlement expiry 28 Apr 2027	Handover completes in Apr 2027
DR site online before DR build and testing	Recovery design now; DR build follows the site

OPEN ITEMS

ITEM	WHAT IT GATES	OWNER
Current RVTools export	Design sign-off and sizing	Pat Rivera

WHO IS INVOLVED

NAME	ROLE	ORGANIZATION
Pat Rivera	Platform lead	Acme Health
Sam Lee	Network	Acme Health
Jordan Blake	Architect	CDW
Casey Morgan	Sr. Consultant	CDW
Alex Kim	PM	Broadcom

ACCEPTANCE

ACME HEALTH

NAME

TITLE

DATE

SIGNATURE

Make Amazing Happen.

CDW · Proprietary and confidential. Copying restricted.
