FUNCTIONAL CONSUMPTION PLAN · SUMMARY

# VMware Cloud Foundation Adoption: Acme Health

**Version 1**
Issued 30 Sep 2026
Prepared by CDW Consulting Solution Architecture

Platform: **VCF 9.1** · Path: **Greenfield with staging hardware** · Delivery: **CDW + Broadcom** · Location: **Reno, NV**

| $79,403 | 223 hrs | 1 Oct 2026 | 28 Apr 2027 |
|---|---|---|---|
| **VCF Services Entitlement** | **Hours Remaining** | **Plan Starts** | **Entitlement Ends** |
| 262 hours · 29 Apr 2026 to 28 Apr 2027 | 39 of 262 delivered as of 3 Sep 2026 | Design and planning first; build from 1 Jan 2027 | Unused hours are not refunded |

## WHAT WE'RE DOING

CDW designs and builds the VCF 9.1 foundation for Acme Health, proves the runbook and hands the platform over. The plan is framed around operations and lifecycle management and resilience and recovery planning, with a separately funded greenfield VCF foundation and workload migration path.

## IN THIS PLAN

- **Program Management & Governance:** Hardware Compatibility Review, Kickoff and Delivery Plan
- **Modernize Infrastructure:** Reference Architecture Design, Migration and Cutover Plan, Greenfield VCF Foundation Build
- **Operations:** VCF Operations Design, Optimization and Advisory Services, Role and Access Mapping, Training and Knowledge Transfer, VCF Operations Licensing, Handover and Service Acceptance
- **Modernize Security & Resilience:** Recovery and Resilience Design

## NOT IN THIS PLAN

- **Modernize Infrastructure:** First Workload Domain, Workload Migration and Cutover, after the entitlement
- **Operations:** Health, Logs, and Diagnostics, Runbook Knowledge Transfer, after the entitlement
- **Modernize Cloud:** not requested (Kubernetes, Private AI and HCX)
- **Modernize Security & Resilience:** Recovery Services Build, after the entitlement
- **Run by Acme Health:** Site prerequisites and hardware evidence; Customer migration waves and legacy cluster retirement

## ARCHITECTURE AT A GLANCE

| | |
|---|---|
| **Platform** | VCF 9.1 on Cisco UCS hosts. Converged management domain: management components and production workloads share the primary cluster. Primary data center and a new DR site. |
| **Storage, network** | Fibre Channel. NSX deployed with VCF, VLAN-backed at first. |
| **Recovery** | DR site as a separate workload domain in the same fleet. |

## WORK PACKAGES

| PACKAGE | MONTH | HOURS |
|---|---|---|
| **DELIVERED TO DATE** | | |
| *Hours delivered to date* | *Apr – Sep 2026* | *39* |
| **PROGRAM MANAGEMENT & GOVERNANCE** | | |
| **Hardware Compatibility Review** | Oct 2026 | 13 |
| **Kickoff and Delivery Plan** | Oct 2026 | 2 |
| **MODERNIZE INFRASTRUCTURE** | | |
| **Reference Architecture Design** | Nov 2026 | 40 |
| **Migration and Cutover Plan** | Dec 2026 | 24 |
| **Greenfield VCF Foundation Build** | Jan 2027 | 63 |
| **OPERATIONS** | | |
| **VCF Operations Design** | Nov 2026 | 10 |
| **Optimization and Advisory Services** | Dec 2026 – Apr 2027 | 6 |
| **Role and Access Mapping** | Dec 2026 | 13 |
| **Training and Knowledge Transfer** | Jan 2027 | 6 |
| **VCF Operations Licensing** | Feb 2027 | 7 |
| **Handover and Service Acceptance** | Apr 2027 | 11 |
| **MODERNIZE SECURITY & RESILIENCE** | | |
| **Recovery and Resilience Design** | Nov 2026 | 10 |
| **Held for change requests, released to follow-on work if unused** | | 18 |
| **Total, funded by the entitlement** | | **262** |


CDW-delivered hours: 39 delivered, 205 planned and 18 held for change requests add up to the 262-hour entitlement. The signed resource assignments replace these estimates.

CDW · Proprietary and confidential. Copying restricted.

# Timeline

1 October 2026 through 28 April 2027, the entitlement window. Dashed bars are run by Acme Health. ◆ marks key delivered functionality.

DELIVERY WORKSTREAM KEY: Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Consume / Handover · Security & Resiliency · Customer-owned · ◆ Checkpoint

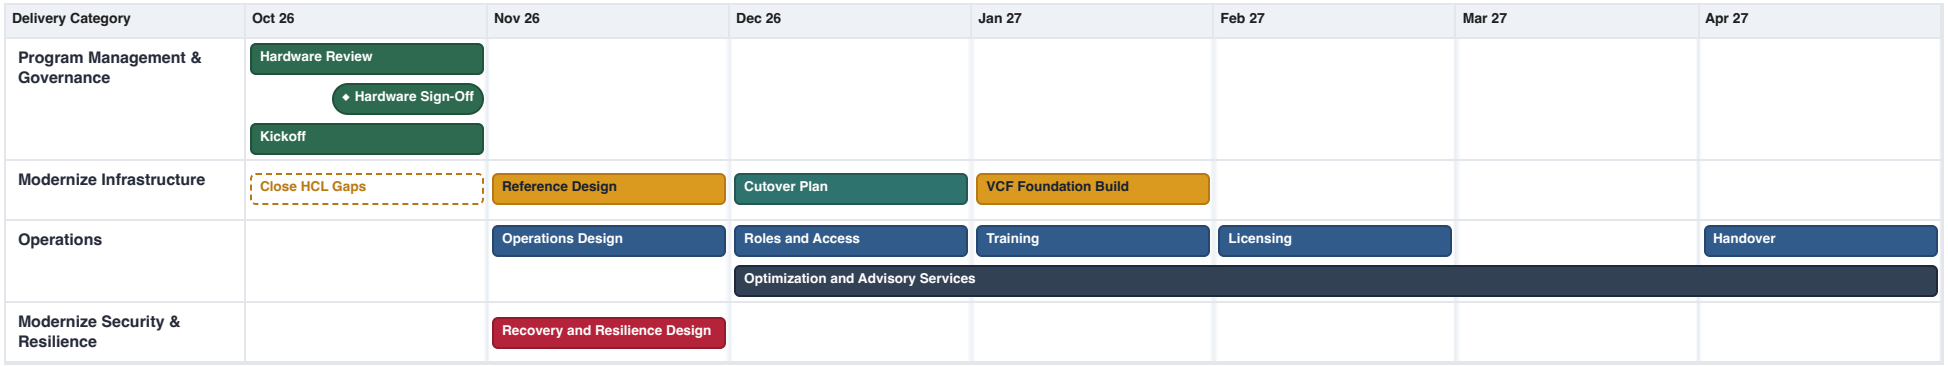


## KEY DATES

| | |
|---|---|
| **1 Oct 2026** | Design and planning start |
| **1 Jan 2027** | Platform build begins |
| **28 Apr 2027** | Entitlement ends; unused hours are not refunded |

## WHAT WE NEED FROM ACME HEALTH

- **Effort:** 6–30 hours per week, peaking at 0.75 FTE during customer-run migration waves
- **Decisions by November:** hosts for the build, DR policy direction, wave ownership

## OPEN ITEMS

| | | |
|---|---|---|
| **Current RVTools export** | Design sign-off and sizing | Pat Rivera |


## AFTER THIS PLAN

> About **323 hours** of follow-on work runs from May 2027. The two-year view and how it's funded are on page 3.

# After the Entitlement

May 2027 through Apr 2028, the second year of the two-year view. This is where Acme Health goes next. None of it is funded by the current entitlement.

DELIVERY WORKSTREAM KEY — Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Consume / Handover · Security & Resiliency · ◆ Checkpoint

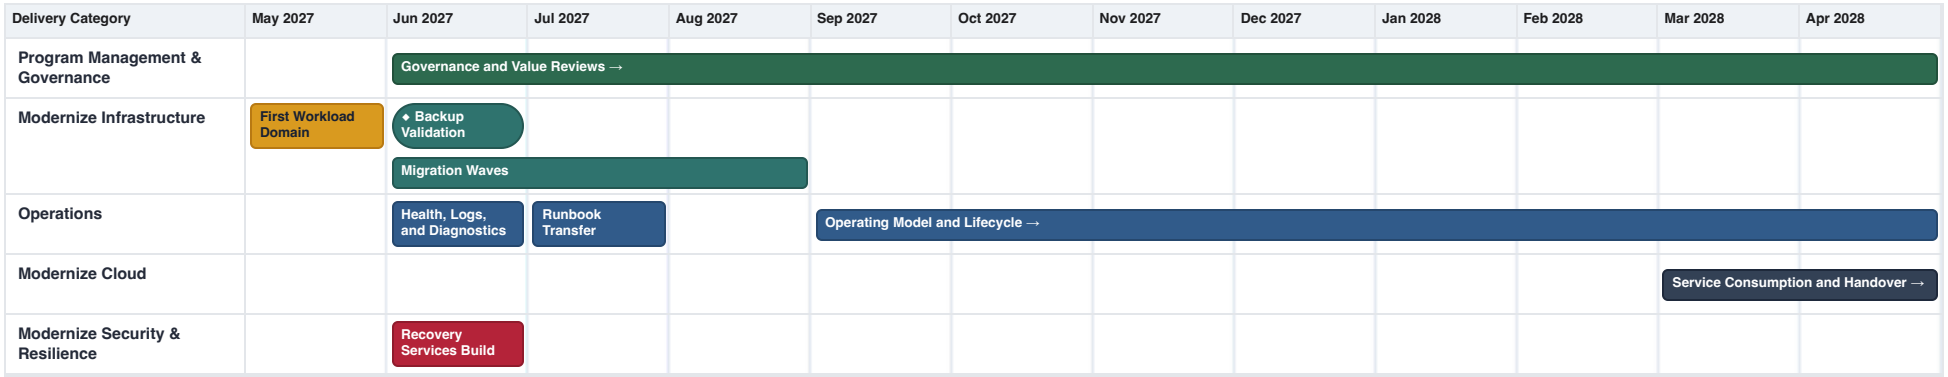


## FOLLOW-ON WORK

| PACKAGE | MONTH | HOURS |
|---|---|---|
| **First Workload Domain**<br>Create the workload-domain foundation used by migration waves and selected component adoption. | May 2027 | 41 |
| **Workload Migration and Cutover**<br>Move the approved workloads, wave by wave, to the accepted VCF foundation and validate service restoration. Accepted when: Each wave meets application, platform, and operational acceptance criteria. | Jun – Aug 2027 | 215 |
| **Health, Logs, and Diagnostics**<br>Implement the selected operating capability with accountable ownership and measurable service outcomes. | Jun 2027 | 30 |
| **Runbook Knowledge Transfer**<br>Hand over the proven migration runbook with shadowed then reverse-shadowed waves, so the team runs the later waves itself. | Jul 2027 | 6 |
| **Recovery Services Build**<br>Implement the selected resilience and security capability with controlled evidence and ownership. | Jun 2027 | 31 |
| **Total follow-on** | | **323** |

Estimated CDW hours, planned against a design already completed in year one.

## HOW IT'S FUNDED

> This work is not drawn from the current entitlement, which ends 28 April 2027.
>
> It needs one of: a renewal with a services entitlement attached, a services purchase, or Broadcom Software Adoption Services hours.

**Make Amazing Happen.**
