FUNCTIONAL CONSUMPTION PLAN

LyondellBasell

A staffing-ready services-entitlement work plan that translates confirmed VCF outcomes into high-level SOW work packages, technical gates, implementation sequencing, and delivery handoff.

Morris, IL | $323,970 | 2025-11-10 to 2026-11-10 | Service delivery & staffing | Technical handoff

Prepared for customer and delivery planning

EXECUTIVE SNAPSHOT

Functional Consumption Plan

A delivery-focused view of confirmed service outcomes, entitlement-bounded execution, and the operational adoption horizon.

ENTITLEMENT VALUE	OBSERVED FOOTPRINT	REPORTED ESXI	DELIVERY POSTURE
$323,970	**2,644 VM records**	**3 releases**	**Implementation-led**
2025-11-10 to 2026-11-10	286 ESXi hosts	VMware ESXi 8.0.3 build-24784735 · 267 hosts; VMware ESXi 8.0.3 build-24859861 · 18 hosts; VMware ESXi 8.0.3 build-24585383 · 1 host	Estate evidence supports validation

CUSTOMER BACKGROUND

LyondellBasell

LyondellBasell is preparing a delivery-led VCF adoption that converts confirmed outcomes into an implementation sequence, operating-model transition, and service handover. The plan is framed around operations and lifecycle management and automation and self-service foundations, with an in-place modernization path. Delivery planning is informed by a current-state estate view used as supporting evidence and validation context, rather than as a completion measure.

LOCATION

Morris, IL

DELIVERY FOCUS

Implementation sequencing, operating-model transition, lifecycle enablement, and service handover

PLANNING BASIS

Entitlement-bounded execution with a two-year operational adoption horizon

PLAN SYNOPSIS

Customer-aligned delivery plan

The plan is framed around operations and lifecycle management and automation and self-service foundations, with an in-place modernization path.

Entitlement Notional: this entitlement-bounded view runs from the planned project start (2026-08-03) through 2026-11-10 and retains only scheduled work that fits within the entitlement period.

Delivery Staffing Timeline: this is the two-year delivery horizon beginning 2026-08-03. It uses weekly execution windows and connects each work package to lead resource guidance, dependencies, gates, and concurrent workstreams.

Plan on a Page

The plan translates selected service outcomes into delivery work, using estate evidence only to inform planning conditions and validation.

Customer and Delivery Summary

01 Customer delivery context

LyondellBasell is preparing a VCF adoption focused on delivering the confirmed platform outcomes through a sequenced implementation, operating-model transition, and service handover. Estate evidence informs delivery conditions and validation; it does not define the customer story or completion measure.

02 Observed footprint

2,644 virtual machines across 286 ESXi hosts, 121 clusters, and 107 datacenters. Reported ESXi: VMware ESXi 8.0.3 build-24784735 (267 hosts); VMware ESXi 8.0.3 build-24859861 (18 hosts); VMware ESXi 8.0.3 build-24585383 (1 host).

03 Selected scope

The plan is framed around operations and lifecycle management and automation and self-service foundations, with an in-place modernization path.

04 Entitlement Notional

$323,970 is available through 2026-11-10. This entitlement-bounded view begins at the planned project start (2026-08-03) and retains only work scheduled within the entitlement period.

05 Delivery Staffing Timeline

A two-year delivery horizon begins 2026-08-03 and uses weekly execution windows. Lead resource roles, staffable work packages, and concurrent delivery workstreams are derived from the authoritative plan.

Timeline Validation

Timeline validation: The current plan is within the configured timeline bounds. Confirm sequencing and prerequisites with the customer before delivery.

VCF 9.1 Readiness

A concise readiness summary for delivery decisions, validation priorities, and mobilisation sequencing.

PRESALES-TO-DELIVERY HANDOFF

ESXi 9.1 compatibility posture

Catalog-versioned server and CPU evidence, current-estate context, release disposition, and owned delivery actions.

TARGET RELEASE LISTED	BLOCKED / NOT LISTED	EVIDENCE REQUIRED	ESTATE RECONCILIATION
276 hosts	**—** hosts	**10** hosts	**Complete** 286 of 286 imported hosts are reconciled to a compatibility cohort.

Maintained evidence baseline

broadcom-server-2026-07-28

3,423 server records across 74 manufacturers; release scope ESXi 9.0 and ESXi 9.1; captured 2026-07-28T17:47:28Z.

Observed ESXi: VMware ESXi 8.0.3 build-24784735 · 267 hosts; VMware ESXi 8.0.3 build-24859861 · 18 hosts; VMware ESXi 8.0.3 build-24585383 · 1 host

Priority delivery actions

1. **8 hosts · Customer infrastructure owner with delivery engineering**
   Confirm the exact OEM server model and CPU, then validate the complete configuration in the Broadcom Compatibility Guide before selecting the VCF path.
2. **2 hosts · Customer infrastructure owner with delivery engineering**
   Confirm the exact OEM server model and CPU, then validate the complete configuration in the Broadcom Compatibility Guide before selecting the VCF path.
3. **276 hosts · Delivery engineering**
   Retain the HCL evidence in the delivery baseline and validate NIC, HBA/controller, firmware, driver, OEM image, storage, vSAN/ReadyNode, build, and topology requirements before deployment.

Server-and-CPU support is one gate. Delivery must also validate NICs, HBAs/controllers, firmware, drivers, OEM image or add-on, boot, storage, vSAN/ReadyNode where applicable, and cluster topology. The standalone compatibility deliverable contains the complete cohort evidence and action register.

Entitlement Notional

Entitlement-period delivery view: This monthly view starts with the planned delivery mobilisation date and ends at the calculated entitlement end date. It includes only service delivery, governance, lifecycle, handover, and selected expansion work that can be completed within that period; it is a planning recommendation, not a commitment of services.


PLANNED DELIVERY START THROUGH ENTITLEMENT END

Entitlement-Aligned Delivery Outlook

Delivery is scheduled from 2026-08-03 through 2026-11-10. The opening and closing month labels show the actual partial-month boundaries so the view can be read as an entitlement-bounded delivery sequence.

DELIVERY WORKSTREAM KEY

- Governance
- Operating Model / Platform
- Infrastructure Build
- Migration Waves
- Consume / Handover
- Security & Resiliency

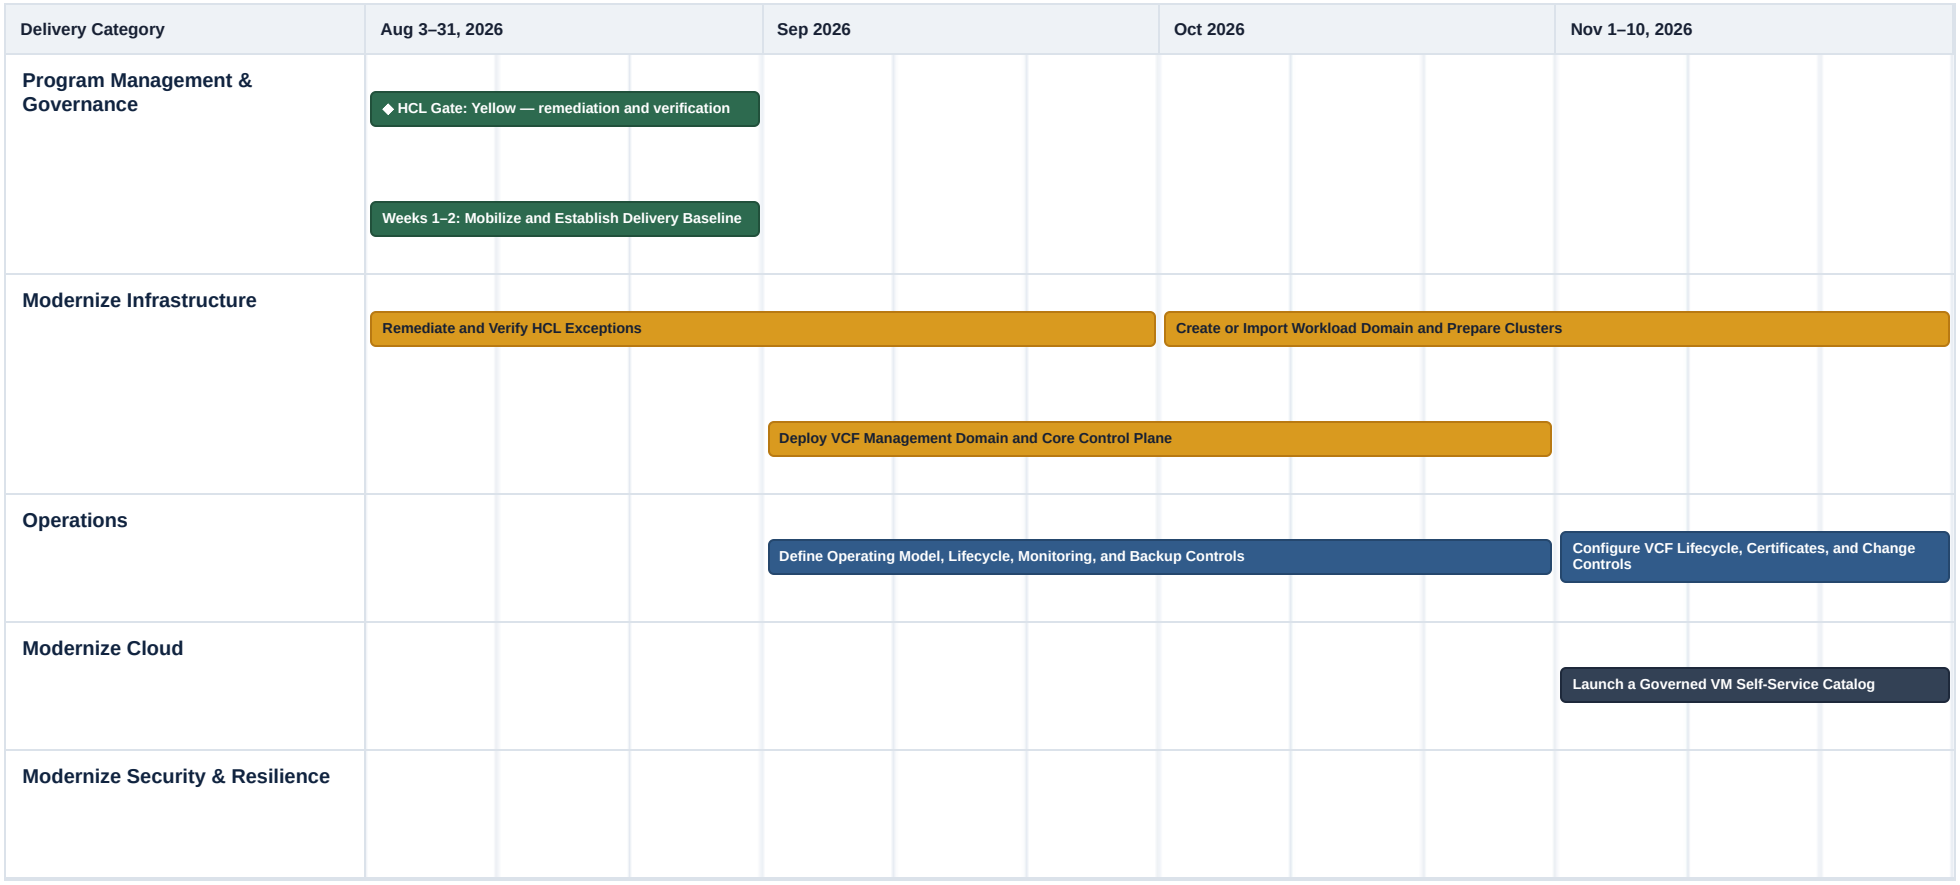

Delivery Staffing Timeline

Delivery resource view: This schedule turns the adoption plan into staffable work packages. Resource roles and calendar windows are planning guidance; delivery leadership validates effort, availability, named resources, and commercials before mobilization.

LEAD DELIVERY ROLES	WORK PACKAGES	PEAK CONCURRENT PACKAGES
5	12	2

Lead Delivery Role	Workstream	Staffing Window	Packages	Planned Work
Engagement Manager / Project Manager	Governance	Aug 3–Aug 9, 26 – Sep 7–Sep 13, 26	2	Weeks 1–2: Mobilize and Establish Delivery Baseline · HCL Gate: Yellow — remediation and verification
VCF Architect + Operations Lead	Operating Model / Platform	Sep 14–Sep 20, 26 – Feb 1–Feb 7, 27	4	Define Operating Model, Lifecycle, Monitoring, and Backup Controls · Configure VCF Lifecycle, Certificates, and Change Controls · Deploy VCF Operations Health, Logs, and Diagnostics · Validate Handover, Service Acceptance, and Ongoing Lifecycle
VCF Implementation Engineer	Infrastructure Build	Aug 17–Aug 23, 26 – Nov 9–Nov 15, 26	3	Remediate and Verify HCL Exceptions · Deploy VCF Management Domain and Core Control Plane · Create or Import Workload Domain and Prepare Clusters
Migration Lead + Application Owners	Migration Waves	Dec 28–Jan 3, 27 – Jan 11–Jan 17, 27	1	Execute VCF 9.1 In-Place Upgrade Waves
Automation / Platform Engineer	Consume / Handover	Nov 16–Nov 22, 26 – Dec 21–Dec 27, 26	2	Launch a Governed VM Self-Service Catalog · Implement Day-2 Remediation and Maintenance Automation

Staffing guidance supports resource planning. Delivery leadership must confirm named resources, effort, utilization, regional availability, customer responsibilities, commercial rates, and formal acceptance criteria before work begins.

OPERATIONAL DELIVERY HORIZON · YEAR 1

Aug 26 through Jun 27

This executive monthly view preserves the full delivery horizon without reproducing detailed weekly execution mechanics. Activities spanning a boundary continue in the next view.

DELIVERY WORKSTREAM KEY: Governance · Operating Model / Platform · Infrastructure Build · Migration Waves · Consume / Handover · Security & Resiliency

Delivery Category	Aug 26	Sep 26	Oct 26	Nov 26	Dec 26	Dec 27	Jan 27	Feb 27	Mar 27	Apr 27	May 27	Jun 27
Program Management & Governance	Weeks 1–2: Mobilize and Establish Delivery Baseline	◆ HCL Gate: Yellow — remediation and verification										
Modernize Infrastructure	Remediate and Verify HCL Exceptions	Deploy VCF Management Domain and Core Control Plane				Execute VCF 9.1 In-Place Upgrade Waves						
			Create or Import Workload Domain and Prepare Clusters									
Operations		Define Operating Model, Lifecycle, Monitoring, and Backup Controls		Configure VCF Lifecycle, Certificates, and Change Controls	Deploy VCF Operations Health, Logs, and Diagnostics		Validate Handover, Service Acceptance, and Ongoing Lifecycle					
Modernize Cloud				Launch a Governed VM Self-Service Catalog	Implement Day-2 Remediation and Maintenance Automation							
Modernize Security & Resilience												

High-Level SOW Work Package Register

The register carries the same authoritative timeline into delivery scope, role ownership, outcomes, dependencies, and assumptions.

Work Package	Lead Delivery Role	Start Week	End Week	Outcome / Acceptance Direction	Dependencies and Assumptions
PROGRAM MANAGEMENT & GOVERNANCE					
Weeks 1–2: Mobilize and Establish Delivery Baseline Governance	Engagement Manager / Project Manager	Aug 3–Aug 9, 26	Aug 10–Aug 16, 26	Time-box the delivery baseline, capture the offline HCL evidence and remaining configuration decisions, then release the management-domain, networking, workload-domain, migration, and handover workstreams for execution.	RVTools identifies 286 observed hosts across 11 host models. HCL schedule path Yellow: Yellow — remediation and verification. The supplied offline HCL snapshot identifies 10 host(s) that need CPU, vendor, or model confirmation before their pairing can be relied upon. Confirm server configuration, CPU, NIC, storage controller, firmware, driver, vSAN/ReadyNode details, bill of materials, and implementation prerequisites before platform deployment begins. Apply the customer-confirmed objectives or constraints: vSAN, NSX and vDefend out of scope. Primary focus is the upgrade to 9.1 and automation. Anything managed by HPE is excluded in the scope as well..
HCL Gate: Yellow — remediation and verification Governance	Engagement Manager / Project Manager	Sep 7–Sep 13, 26	Sep 7–Sep 13, 26	Authorize foundation work only after the required HCL path evidence is recorded.	2.0.0 Yellow — remediation and verification gate closes only after remediation or evidence review is accepted.
MODERNIZE INFRASTRUCTURE					
Remediate and Verify HCL Exceptions Infrastructure Build	VCF Implementation Engineer	Aug 17–Aug 23, 26	Aug 31–Sep 6, 26	Close the reported HCL exception path and retain verification evidence.	Resolve server, CPU, firmware, or identity evidence before releasing the platform build. Apply the customer-confirmed objectives or constraints: vSAN, NSX and vDefend out of scope. Primary focus is the upgrade to 9.1 and automation. Anything managed by HPE is excluded in the scope as well..
Deploy VCF Management Domain and Core Control Plane Infrastructure Build	VCF Implementation Engineer	Sep 14–Sep 20, 26	Oct 5–Oct 11, 26	Deploy the VCF management domain and validate core platform health.	Begin after the HCL gate, mobilisation baseline, bill of materials, and platform prerequisites are accepted.

Work Package	Lead Delivery Role	Start Week	End Week	Outcome / Acceptance Direction	Dependencies and Assumptions
Create or Import Workload Domain and Prepare Clusters Infrastructure Build	VCF Implementation Engineer	Oct 12–Oct 18, 26	Nov 9–Nov 15, 26	Create or import the workload domain and prepare the foundation used by migration and selected module work.	Begin after management-domain health and the applicable platform prerequisites are validated.
Execute VCF 9.1 In-Place Upgrade Waves Migration Waves	Migration Lead + Application Owners	Dec 28–Jan 3, 27	Jan 11–Jan 17, 27	The in-place path sequences controlled VCF 9.1 upgrade waves with rollback and post-wave health checks.	Begin only after selected Cloud and Security & Resilience activities complete, as well as workload-domain readiness, application dependency review, rollback planning, and change-window approval. Apply the customer-confirmed objectives or constraints: vSAN, NSX and vDefend out of scope. Primary focus is the upgrade to 9.1 and automation. Anything managed by HPE is excluded in the scope as well..
OPERATIONS					
Define Operating Model, Lifecycle, Monitoring, and Backup Controls Operating Model / Platform	VCF Architect + Operations Lead	Sep 14–Sep 20, 26	Oct 5–Oct 11, 26	Set operating ownership, lifecycle controls, monitoring, backup, and service-management expectations.	Begin after the HCL gate and run in parallel with the VCF foundation build.
Configure VCF Lifecycle, Certificates, and Change Controls Operating Model / Platform	VCF Architect + Operations Lead	Nov 16–Nov 22, 26	Nov 30–Dec 6, 26	Implement the selected operating capability with accountable ownership and measurable service outcomes.	Begin after workload-domain readiness and the HCL gate.
Deploy VCF Operations Health, Logs, and Diagnostics Operating Model / Platform	VCF Architect + Operations Lead	Dec 7–Dec 13, 26	Dec 21–Dec 27, 26	Implement the selected operating capability with accountable ownership and measurable service outcomes.	Begin after workload-domain readiness and the HCL gate.
Validate Handover, Service Acceptance, and Ongoing Lifecycle Operating Model / Platform	VCF Architect + Operations Lead	Jan 18–Jan 24, 27	Feb 1–Feb 7, 27	Confirm operational readiness, evidence, ownership, and the continuing lifecycle cadence.	Begin after the final migration or implementation wave is accepted.
MODERNIZE CLOUD					
Launch a Governed VM Self-Service Catalog Consume / Handover	Automation / Platform Engineer	Nov 16–Nov 22, 26	Nov 30–Dec 6, 26	Enable the confirmed cloud capability on the accepted VCF foundation.	Begin after workload-domain readiness and the HCL gate.
Implement Day-2 Remediation and Maintenance Automation Consume / Handover	Automation / Platform Engineer	Dec 7–Dec 13, 26	Dec 21–Dec 27, 26	Enable the confirmed cloud capability on the accepted VCF foundation.	Begin after workload-domain readiness and the HCL gate.
MODERNIZE SECURITY & RESILIENCE					
